InvestFlow Digital Customer Experience Redesign

Deepika Kola | Portfolio case study | November 2026

InvestFlow is an independently developed simulated portfolio project. It uses demo investment data and role placeholders. No financial institution sponsored the work. The project involved no customer research, live trading, production release, or measured customer impact.

Executive summary

A retail investing customer needs to answer three questions before taking action: what is available now, what changed over time, and what am I about to confirm? InvestFlow makes those decisions easier to evaluate by separating balances, synchronizing performance periods, and clearing old order confirmations after edits.

I connected the delivery plan in Wrike to the requirements, prototype and browser evidence. I used AI assistance for drafting, configuration, implementation and test execution. The strongest example is order review. The first version could show a previous confirmation beside a newly edited order. The updated version clears that confirmation and requires a new review.

Backlog scope	Estimated effort	Review gates	Schedule links
47 delivery tasks	143 story points	7 native milestones	12 finish-to-start dependencies

Evidence at a glance

Evidence	What it demonstrates
Requirements and traceability	Ten pain points linked to requirements, story IDs, screens, tests, and results.
Prototype and retest	Five original failures reproduced and retested. 23 of 23 checks passed in Chromium and 23 of 23 passed in Firefox.
Delivery governance	Six sprint groups, the schedule reconciliation, and a readiness decision that separates prototype evidence from release acceptance.

Outcome and boundary

The revised prototype is ready for a portfolio walkthrough. Release acceptance remains open because accessibility, customer validation, and live Wrike reconciliation are incomplete.

Journey hypotheses and decisions

Three personas guided the test design. They represent plausible behavior for this exercise. Their needs have yet to be validated with participants.

Persona	Decision they need to make	Risk if the design is unclear
New investor	Distinguish invested assets, cash and total balance.	They may confuse portfolio value with money available to use.
Self-directed investor	Find a company, save it, then return to the same result.	An unclear saved state or lost focus can break the research flow.
Active investor	Verify the cost and current terms before confirming.	An old confirmation can appear to validate new inputs.

Journey	Baseline friction or hypothesis	Updated design
Overview	Total reconciled but the screen had no as-of date.	A fixed demo timestamp sits alongside the total and cash breakdown.
Portfolio	The period changed the numbers without a corresponding trend.	The label, amount, plot and table update from the same sample series.
Research and Watchlist	Saving rebuilt the result and sent focus to the page body.	Saving updates the same control. Removing an item moves focus to the next useful control.
Order review	After edits, the previous confirmation remained on screen.	Editing the security or quantity invalidates confirmation immediately.

How to validate the hypotheses

Ask participants to identify available cash, explain a selected return period, find a saved ticker, and revise an order. Record task completion, interpretation accuracy and help needed separately. The browser tests establish behavior under defined inputs. They do not establish customer preference or comprehension.

Requirements traceability

Each row links a customer concern to a business requirement, backlog story, screen and test. The workbook carries the full criteria and both browser results.

Customer concern	Requirement and story	Screen	Executed evidence
Balance freshness	BR01 / IF-010, IF-012, IF-013	Overview	B02. Snapshot and totals verified.
Trend integrity	BR03 / IF-016, IF-017	Portfolio	B03, B04. Values and chart move together.
Research continuity	BR04, BR05 / IF-024 to IF-026, IF-030	Research / Watchlist	B05 to B07, B11. Search and save verified.
Confirmation accuracy	BR06 / IF-033, IF-035, IF-036	Order review	B08 to B10, A08. Edits and errors verified.
Keyboard and mobile access	BR02, BR07 / IF-011, IF-026, IF-040, IF-041	Across views	A01 to A07, A09, M01, M02. Scoped checks passed.

Functional and quality requirements

Functional criteria define what changes, such as the estimate and confirmation when quantity changes. Quality criteria define how it must behave, such as a visible focus outline, an announced selection state and a layout that fits a narrow viewport. The browser register records both the expected and observed behavior.

Prioritization

Prioritize by consequence, reach and evidence. An inconsistent confirmation can misstate the review result, and focus loss blocks keyboard continuity. Comparison, notes and cost basis add value but are separate scope decisions. Preserve those backlog items and assess them before assigning effort or dates.

Balances and performance

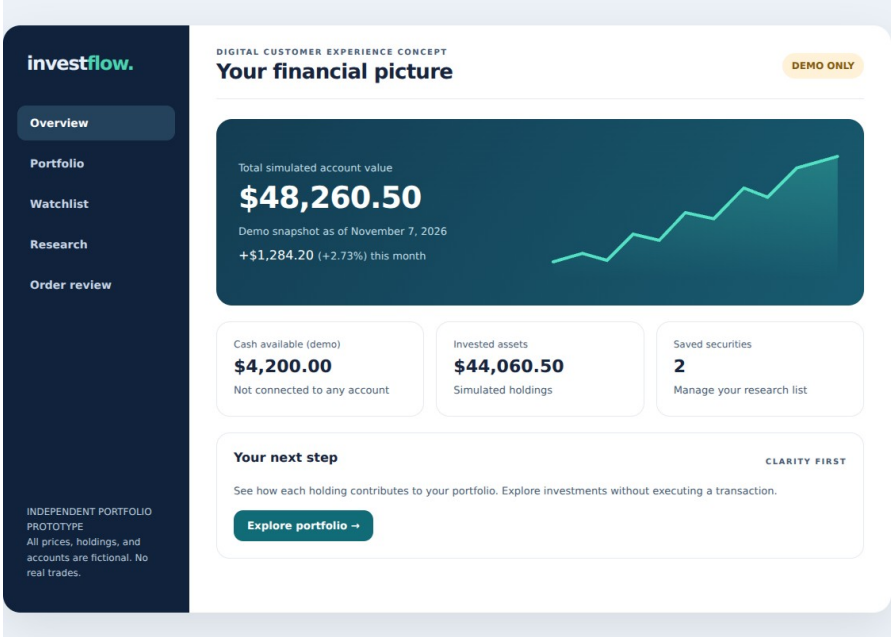


Figure 1. Updated Overview showing the dated demo snapshot and the balance components.

The account summary places cash and invested assets beside the total. The as-of date clarifies freshness without implying a live price feed.

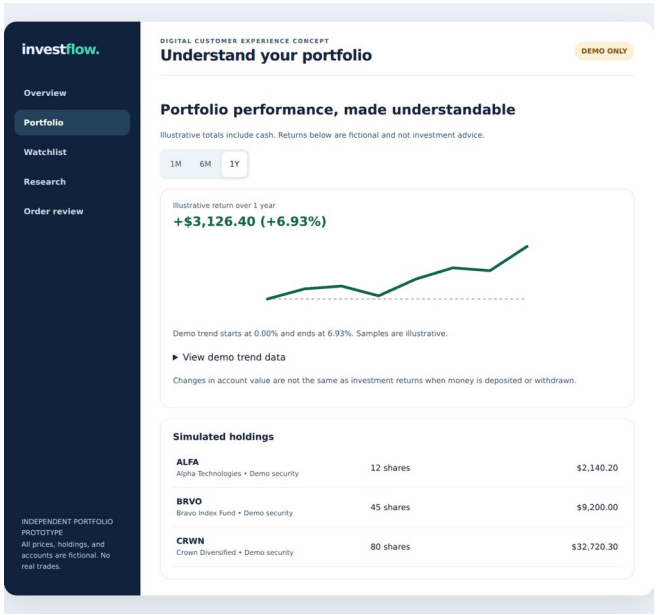


Figure 2. Updated Portfolio with the 1-year return, matching trend and access to the data table.

One period record drives the return label, amount, chart and alternative table. The data table gives users a direct way to verify the displayed samples.

Research and order review

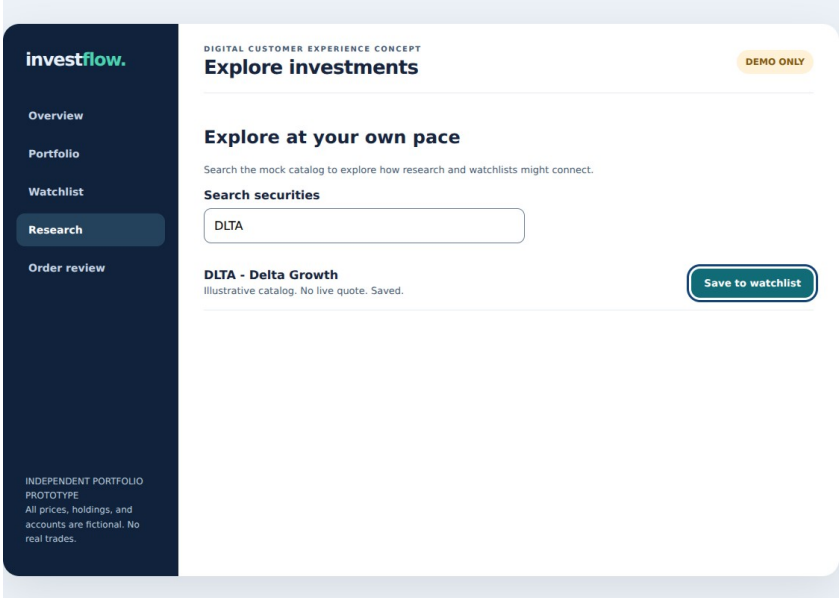


Figure 3. Keyboard focus remains on the DLTA control after a save. The row reports its saved state.

Saving updates the existing button. When a user removes an item, focus moves to the next item or the discovery action. The watchlist lasts for the current page session, as disclosed in the interface.

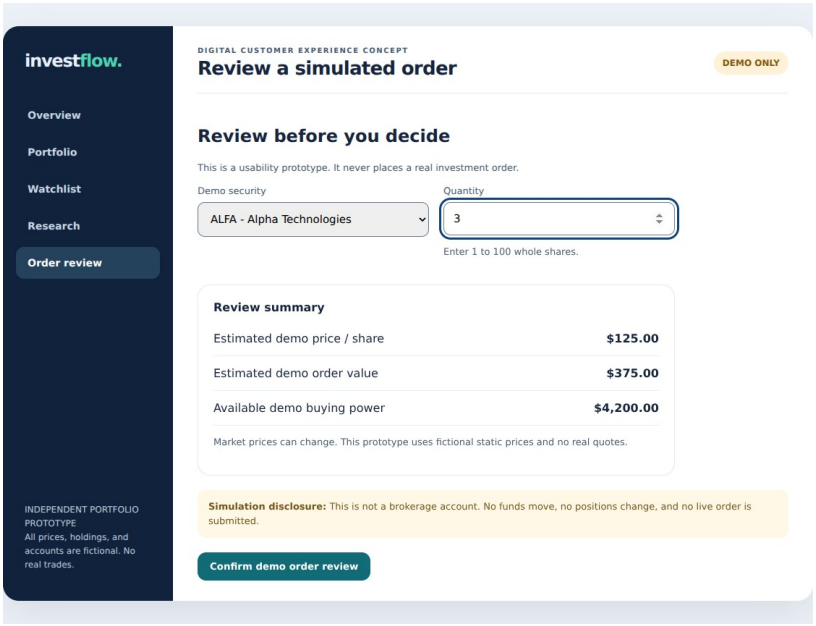


Figure 4. After editing ALFA from two to three shares, the estimate changes to $375 and the old confirmation clears.

The order uses integer cents for the estimate. It rejects invalid quantities and orders above demo buying power. These decisions reduce ambiguity at the point of review and leave a clear test for every input change.

Sprint plan and release gates

The delivery plan has one discovery sprint and five delivery sprints. Story points express planned relative effort. The archived export places all 47 original delivery tasks in Backlog.

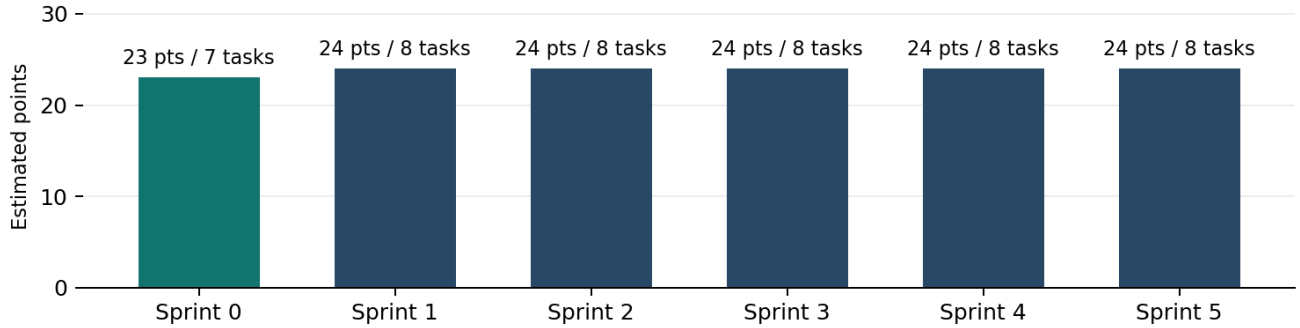


Figure 5. Estimated scope by sprint from the archived Wrike export.

Milestone gate	Task	Planned date
Discovery readiness	IF-006	Nov 27, 2026
Navigation review	IF-015	Dec 11, 2026
Portfolio review	IF-023	Dec 25, 2026
Watchlist review	IF-031	Jan 8, 2027
Order review	IF-039	Jan 22, 2027
Release decision	IF-046	Feb 5, 2027
Portfolio closure	IF-047	Feb 5, 2027

Workflow and sprint review

Backlog, Ready for Sprint, In Progress, Review / UAT, Done (Accepted), and Blocked form the delivery workflow. In a planned review, demonstrate acceptance criteria against the test record and record what was accepted, deferred or sent back. The ceremonies are planning artifacts. No team sessions or sprint acceptance are recorded.

06 WRIKE EVIDENCE

Schedule and governance

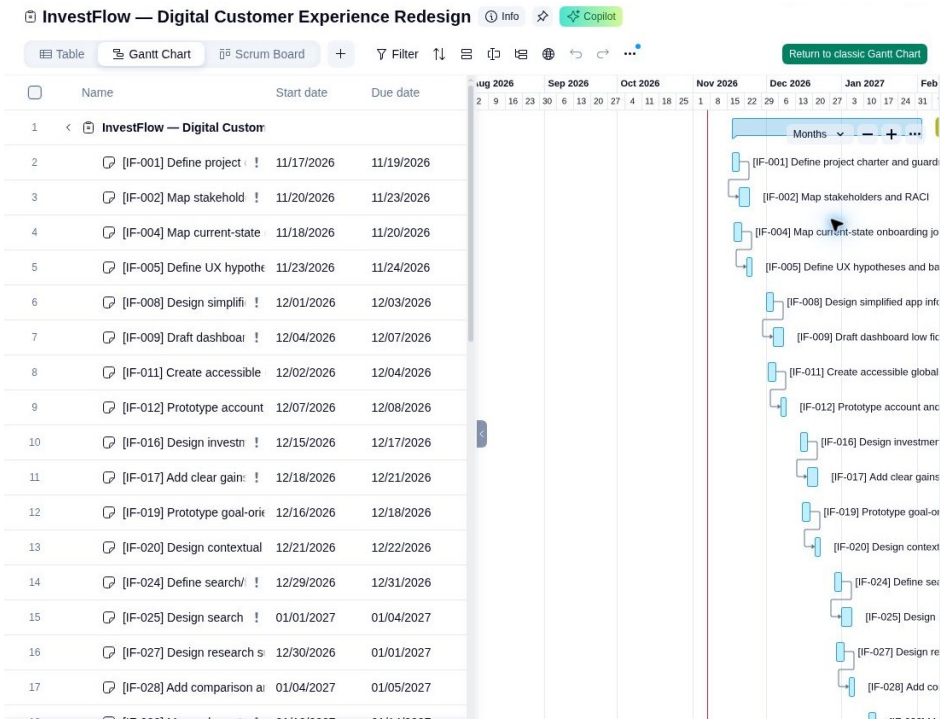


Figure 6. Archived Wrike Gantt capture with dependency links. Cropped to show the schedule without the onboarding pop-up.

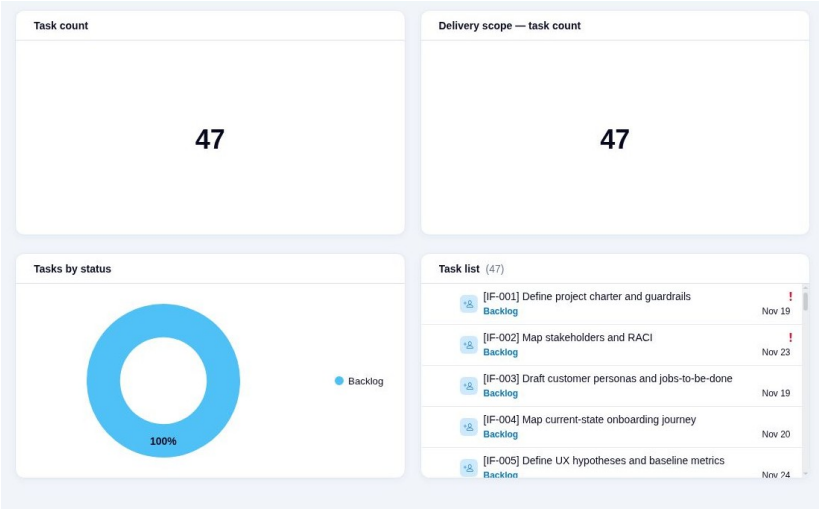


Figure 7. Archived dashboard showing the 47 original delivery tasks before governance subitems were added.

The last verified export reconciles 12 finish-to-start dependencies and 12 changes to imported task dates. Five risks and five issues appear as separate governance subitems. Current live statuses and updated defect records still require Wrike access.

07 VALIDATION

Baseline failures and verified retest

Original failure	Fix	Retest
B02 Missing snapshot date	Add visible, fixed demo as-of date.	Pass in both
B04 Missing period trend	Bind the SVG, endpoint and data table to the period.	Pass in both
B10 Stale order confirmation	Clear confirmation when ticker or quantity changes.	Pass in both
A03 Selected state only visual	Expose current view and pressed period programmatically.	Pass in both
A04 Focus loss after save	Update the saved button in place.	Pass in both

Test conditions and findings

23 of 23 checks passed in Chromium and 23 of 23 passed in Firefox. The suite covers order boundaries and errors, keyboard-only use, explicit labels, holdings reconciliation, search, watchlists, and 320 px and 390 px viewports. Chromium used touch emulation. Firefox used narrow desktop viewports.

Axe reported zero violations among selected rules across all five views in each engine. The Overview gradient remained an incomplete automated item. A separate computed check sampled the two foregrounds against the lighter gradient endpoint and returned 7.58:1 and 5.27:1.

Coverage limits

Screen-reader testing, physical mobile devices, Safari and customer sessions remain unexecuted. The contrast sample and automated scans cover the tested states. They do not establish WCAG conformance.

Decisions and next steps

Workstream	Evidence and decision
Wrike configuration	Archived evidence confirms scope, sprint groups, epics, points and scheduling. Current live state could not be checked because the session required sign-in.
Prototype development	The five baseline defects were corrected. The public demo is ready for a portfolio walkthrough.
Executed testing	Both browser runs passed the defined checks. The report separates automated findings and manual follow-up.
Simulated Agile activities	Sprint plans, review agenda, risk tracking and milestone criteria describe the intended delivery process.
Unexecuted work	Screen reader and physical-device testing, customer validation, holiday capacity review, release sign-off and live Wrike defect updates remain open.

Trade-offs and follow-up

The chart uses deterministic samples so reviewers can reproduce period changes. The watchlist is session-only so the demo needs no storage or accounts. Research comparison, cost basis and loading or cancellation scenarios stay in the register as separate scope items.

Before a production acceptance decision, validate interpretation with participants, run assistive-technology and physical-device checks, and assign owners to the remaining scope. In Wrike, attach the retest evidence to the existing stories and review the calendar before approving dates.

Lesson learned

A passing happy path can conceal a defect in the next action. Testing an edit after confirmation and a save followed by another keyboard action exposed problems that a one-click test would miss.
